ID	Task Name	Duration	Start
1			
2	T1-Q13-XU photgr. targets ready	0 days	Fri 15/06/07
3			
4	Photogr. both sides T1-Q13-XU	2 days	Fri 15/06/07
5	Complete phot. Targets all frames	4 days	Tue 19/06/07
6	Phot. Survey T3-Q13-VX	1 day	Mon 25/06/07
7	Phot. Survey T1-Q02-XU	1 day	Tue 26/06/07
8	Phot. Survey T3-Q02-VX	1 day	Wed 27/06/07
9			
10	Remove beam pipe protection	0 days	Fri 29/06/07
11			
12	Align T2-Q13-XU	3 days	Fri 29/06/07
13	Align T2-Q02-XU	3 days	Wed 04/07/07
14	Check reproducibility T2-XU	2 days	Mon 09/07/07
15	Phot. T2-Q13-XU in situ	2 days	Wed 11/07/07
16			
17	Align T2-Q13-VX	2 days	Fri 13/07/07
18	Align T2-Q02-VX	2 days	Tue 17/07/07
19			
20	Align T3-Q13-VX	4 days	Thu 19/07/07
21	Align T3-Q02-XU	2 days	Wed 08/08/07
22			
23	Summer Holidays	25 days	Thu 02/08/07
24			
25	Magnet test	0 days	Fri 07/09/07
26	Check Bridge position wrt magnet	3 days	Fri 07/09/07
27			
28	Complete alignment of Cframes	25 days	Wed 12/09/07
29			
30	Complete photogr. Cframes	10 days	Wed 17/10/07

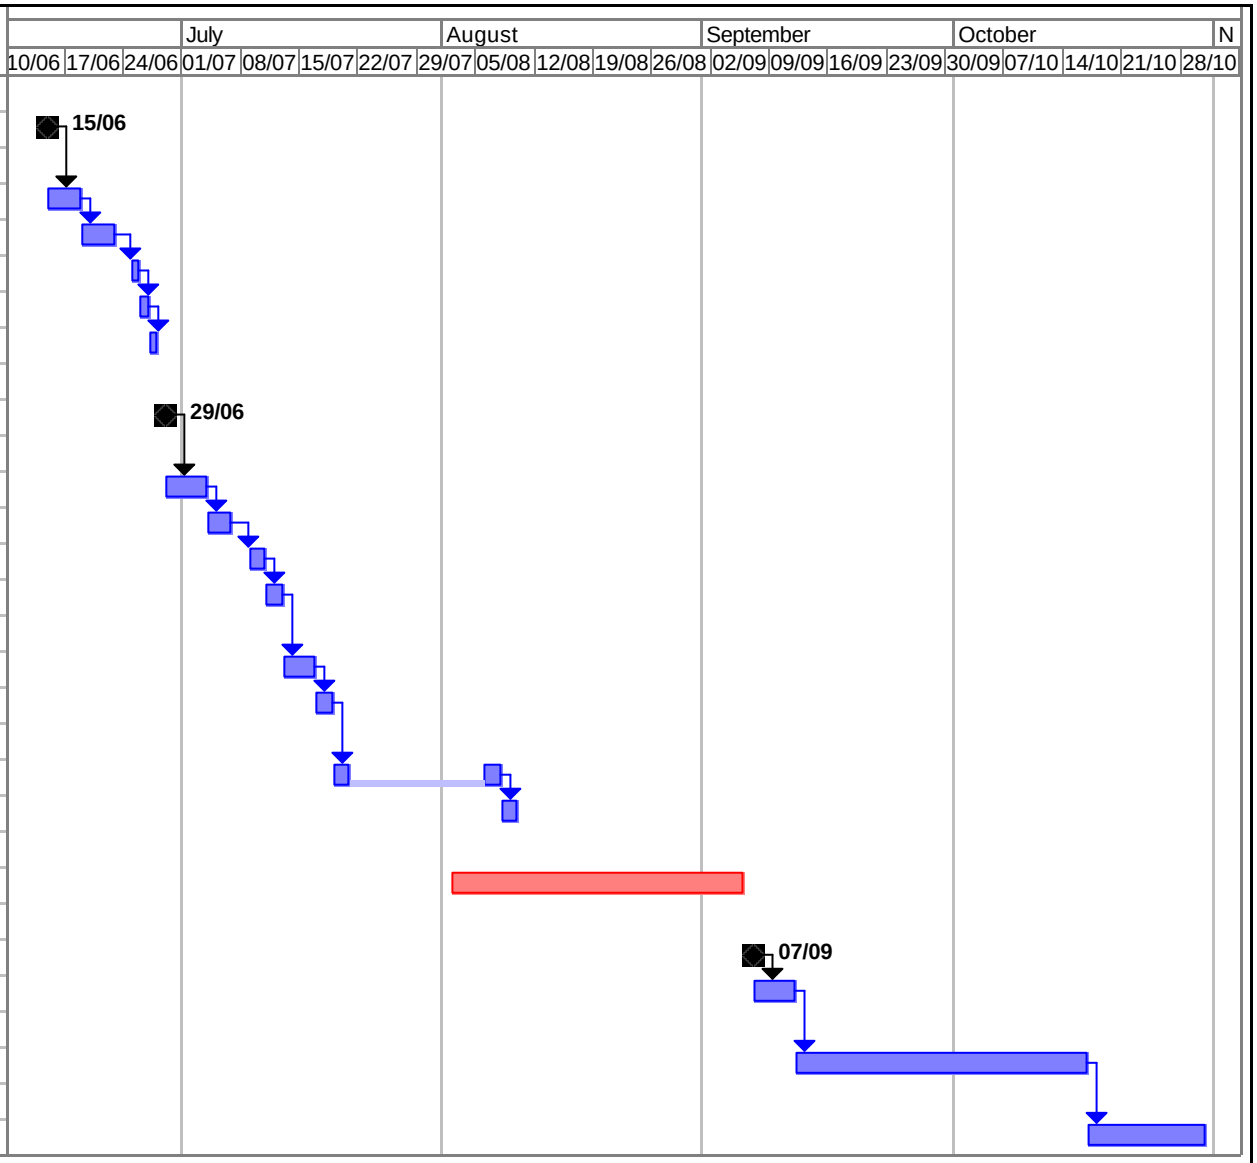

Project: Electronics
Date: Tue 12/06/07

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
